



**LEPL MUNICIPAL DEVELOPMENT  
FUND OF GEORGIA**

**Construction of the village Gvimriani Public School  
(Lagodekhi Municipality)**

**Environmental and Social Screening Report and  
Environmental and Social Management Plan**

**WORLD BANK FINANCED  
INNOVATION, INCLUSION AND QUALITY PROJECT (GEORGIA I2Q PROJECT)**

**Tbilisi, Georgia**

**Updated on June 2025**

### **Sub-project Description**

Construction of the village Gvimriani Public School in Lagodekhi Municipality is one of the sub-projects (SP) to be implemented under the Innovation, Inclusion and Quality Project (Georgia I2Q Project).

The SP site is located in the village of Gvimriani, Lagodekhi Municipality (the land plot is under state ownership cadastral code 54.13.57.223) and covers an area of 23,674 m<sup>2</sup>. The distance from Tbilisi is approximately 130 km. An old school building is located on the land plot designated for the construction of the new school building. As part of this SP, the demolition of the old school building is not planned. It will be fenced off from the construction area and educational activities will continue there. The nearest residential house is about 15 meters away from the land plot allocated for the school. The land plot where the school construction is planned, is a flat area. To the west, it borders a local road, while on the other sides, it is adjacent to privately owned land plots. The area is enclosed by a metal fence.

In accordance with the revised scheme of seismic regions of the territory of Georgia, the SP site falls in the 9-point seismic activity zone according to the MSK64 scale (Order of the Minister of Economic Development of Georgia No. 1-1/2284, October 7, 2009).

According to the design, the school building will be two-storied with the total area of 2,726.36 m<sup>2</sup> and will accommodate 100 students. The first floor of the school building will comprise the main hallway, the buffet, classrooms for grades 1–5, storage rooms for classrooms, a security room, room with storage and sanitary facilities, a music room, a medical room with an isolation area, a multipurpose room, a resource room, the director's office, boys' and girls' restrooms, staff restrooms, a large multipurpose room, an art and applied arts room, a studio, a school warehouse, and a maintenance room for school infrastructure.

The second floor will include classrooms for grades 5–12, storage rooms for classrooms, a staff lounge, a science laboratory with a support storage room, boys' and girls' restrooms, restrooms with universal access, an IT classroom, a library, an advanced IT (information technology) classroom for higher grades, a server room, and a multipurpose hall with lockers.

The design ensures a modern, functional, and accessible educational environment, meeting the diverse academic and extracurricular needs of students and staff. In accordance with the design specifications, the entire infrastructure will accommodate individuals with disabilities and other special needs. The building will include emergency exits, two stairwells, and one elevator to ensure accessibility and safety.

Gvimriani Village is provided with limited utility services, including electricity and natural gas. No potable water supply or wastewater collection and treatment systems are in place. The existing school is supplied with drinking water from a well in the schoolyard. The same well will be used for the new school. Gvimriani Village residents use pit toilets. SP will provide the new school building with the autonomous biological treatment system for sewage management.

The SP foresees the implementation of the following works:

- Preparatory works: Installation of temporary structures such as WCs, lockers for the workers, guard booth, storages for materials as well as household and hazardous waste disposal sites);
- Construction of the main building;
- Construction of the boiler;
- Installation of a biological treatment unit for receiving sewage;
- Installation of internal networks for water supply, electricity and gas supply, heating and ventilation networks;
- Installation of external gas supply and internet networks and connecting of them to the existing municipal networks;
- Installation of fire alarm and firefighting systems;

- Arrangement of playgrounds with artificial covers;
- Fencing the territory;
- Arrangement of parking lots.

There are several trees and bushes in the school yard. According to the design, there is no need to cut them for the construction of the school building, boiler room, playgrounds and paths. As a result of the construction works, it is expected that 1,500 m<sup>3</sup> of cut soil will be generated, of which 500 m<sup>3</sup> will be reused for backfilling and the rest will be removed to a sanitary landfill operated by Solid Waste Management Company of Georgia based on the agreement with this Company or disposed to a site to be allocated by the municipal authority. Also, the removal of 350 m<sup>3</sup> topsoil will be required, which will be temporarily stored on the school territory (construction site) in accordance with the requirements stipulated of the technical regulations approved by the Resolution N424 of the Government of Georgia, dated December 31, 2013, on the Removal, Storage, Use, and Reclamation of Topsoil. After the construction, topsoil will be reused for landscaping of the school area.

## Environmental Screening and Classification of Subprojects

### (A) IMPACT IDENTIFICATION

Does the sub-project have tangible impact on the environment?	<p>The SP will have a modest negative environmental impact.</p> <p>The main impact will be related to the demolishing and construction phase, which includes construction of the school and boiler building and arrangement of playgrounds with artificial covers.</p>
What are the significant beneficial and adverse environmental effects of sub-project?	<p>The expected negative environmental impact will have short-term character and will be typical for small-scale construction works in modified landscape: noise, dust, vibration, and emissions from the operation of construction machinery; generation of construction waste. The later impacts are related to the generation of waste from maintenance of the school which will be managed by the local municipality.</p> <p>The SP site is located in the area with modified environment. Therefore, the impact will be transitory and insignificant (noise, emissions, construction waste, temporary disturbance of traffic and access, etc.).</p> <p>In operation, proper management of generated solid waste should be ensured to reduce impact on the environment.</p>
May the sub-project have any significant impact on the local communities and other affected people?	<p>The SP is expected to have a long-term positive social impact, as the local residents will be able to have access to the modern school, which will be also adapted to the people with disabilities.</p> <p>Ultimate goal of the SP is to improve the quality and conditions of education for children in village Gvimriani. Construction of the school will bring immediate benefits to its users through improved learning spaces, playgrounds, everyday learning activities and in general infrastructure and living conditions. The long-term social impact will be beneficial, as local children and teachers in school will be provided with improved educational and working conditions, increased income of population during the implementation (employment of workers), and after the construction.</p> <p>The SP will create temporary and some permanent job opportunities for the local population (both men and women), as they could be employed during construction and maintenance. Availability of modern school in the community will allow more people (especially those having school age children) to stay in the village Gvimriani.</p> <p>Negative impact is short term and limited to the construction site. It is related to the possible disturbance described above.</p> <p>The SP envisages adaption of the school building to make available servicing of people with disabilities.</p> <p>The SP doesn't envisage land take or resettlement, as well as economic displacement (for example, for formal or informal vendors).</p>

## (B) MITIGATION MEASURES

Were there any alternatives to the sub-project design considered?	No design alternatives were considered at the screening stage, because the school building is yet to be designed under the Design-Build Contract. School design will meet national standards adopted for school buildings and the best feasible alternatives will be selected for design features that may be adjusted to individual locations and demand.
What types of mitigation measures are proposed?	<p>The expected negative impacts of the construction phase can be easily mitigated through proper management of construction activities. The contractor will be responsible for the waste disposal at the permitted location, use the quarry materials from the licensed quarries only or obtain materials only from licensed providers, prevent water and soil from pollution (fuel spills due to equipment failure, concrete spills etc.), avoid disturbance of population (noise, dust, emissions) through proper work/supplies scheduling, traffic management, and good maintenance of the construction machinery.</p> <p>Inspection of vehicles will be required to ensure that there is no leakage of fuel and lubricating materials, all machinery will be maintained and operated such that all leaks and spills of materials will be minimized, the contractor will be required to organize and cover material storage areas. The material storage sites will be protected from washing out during heavy rainfalls and flooding through covering by impermeable materials; car maintenance points will not be located within 50 m of any watercourse.</p> <p>During SP implementation, warning signs will be used, and traffic will be managed around the work sites.</p> <p>Handling of asbestos-containing waste will require much attention to prevent damage to health and safety of workers, nearby communities, and pollution of the environment. Disciplined use of personal protective equipment, watering of the worksite, separate safe on-site storage of hazardous waste, and its timely disposal to the designated landfill operated by the Solid Waste Management Company of Georgia will be applied as mitigation measures. Local residents will be warned on the health risks associated with the re-use of asbestos-containing material and their agreement to allow disposal of such material will be secured.</p> <p>Community health and safety will be an issue during the construction phase as residential buildings are located near the SP site. The contractor will be responsible for taking specific measures to mitigate the impact on locals, including informing the affected population on the upcoming works and any temporary disruptions of municipal services, limiting working hours to daytime, limiting the speed of moving construction vehicles &amp; machinery, minimizing noise &amp; dust emissions, etc.</p> <p>No major hazards are expected during the construction works, as long as proper construction practices and safety procedures are applied.</p> <p>There are grass cover and topsoil layer on the designing territory. The revealed topsoil will be fully re-used for the landscaping. Before commencing the soil works, cleaning of designing territory from grass-type plants, topsoil will be removed and temporary stored.</p>

What lessons from the previous similar projects have been incorporated into the sub-project design?	<p>The Municipal Development Fund of Georgia (MDF) has a broad experience in the implementation of reconstruction / rehabilitation for medium and large-scale buildings (including public schools and kindergartens) roads and streets financed by various donor organizations. Based on lessons learned from previous similar projects, design envisages not only the construction of the school, but also the improvement of heating, ventilation and fire control system, hot water supply, lighting systems and reference energy saving potential, implementation of energy efficiency improvement measures.</p> <p>The infrastructure of the school will be adapted for receiving and servicing of people with disabilities.</p>
Have concerned communities been involved and have their interests and knowledge been adequately taken into consideration in sub-project preparation?	<p>The SP has been developed by the MESY, together with local resource center, as a response to the current situation.</p> <p>An Environmental and Social Management Plan (ESMP) to be drafted for the SP will be made available for the beneficiaries and other interested parties and will be discussed in a consultation meeting.</p> <p>Information about the public consultation meeting will be announced both on the official websites of the MDF and MESY, as well as on the information boards of the school and the local municipality building.</p> <p>The public discussion will be organized by MDF and MESY. The public discussion will be attended by all the interested parties, including parents of the school students. Information about the exact time and place of the public consultation meeting will be announced at least 10 days prior.</p>

#### (C) CATEGORIZATION AND CONCLUSION

1. Subproject is declined ☐
2. Subproject is accepted ☒

Subproject preparation requires:

1. Completion of the Environmental and Social Management Checklist for Small Construction and Rehabilitation Activities ☒
2. Environmental and Social Review, including development of Environmental and Social Management Plan ☐

### Social and Cultural Resource Screening of SP

Social safeguards screening information		Yes	No
1	Is the information related to the affiliation, ownership and land use status of the sub-project site available and verifiable? (The screening cannot be completed until this is available)	X	
2	Will the sub-project reduce people's access to their economic resources, such as land, pasture, water, public services, sites of common public use or other resources that they depend on?		X
3	Will the sub-project result in resettlement of individuals or families or require the acquisition of land (public or private, temporarily or permanently) for its development?		X
4	Will the project result in the temporary or permanent loss of crops, fruit trees and household infra-structure (such as ancillary facilities, fence, canal, granaries, outside toilets and kitchens, etc.)?		X
If answer to any above question (except question 1) is "Yes", then <b>OP/BP 4.12 Involuntary Resettlement</b> is applicable and mitigation measures should follow this OP/BP 4.12 and the resettlement PolicyFramework			
Cultural resources safeguard screening information		Yes	No
5	Will the project require excavation near any historical, archaeological or cultural heritage site?		X
If answer to question 5 is "Yes", then <b>OP/BP 4.11 Physical Cultural Resources</b> is applicable and possiblechance finds must be handled in accordance with OP/BP and relevant procedures provided in the Environmental and Social Management Framework.			

## Environmental and Social Management Plan

### PART A: GENERAL PROJECT AND SITE INFORMATION

INSTITUTIONAL & ADMINISTRATIVE	
<b>Country</b>	Georgia
<b>Project title</b>	INNOVATION, INCLUSION AND QUALITY PROJECT (GEORGIA I2Q PROJECT)
<b>Sub-Project title</b>	Construction of the public school in village Gvimriani
<b>Scope of site-specific activity</b>	<p>Construction of the village Gvimriani Public School in Lagodekhi Municipality is one of the sub-projects (SP) to be implemented under the Innovation, Inclusion and Quality Project (Georgia I2Q Project).</p> <p>The SP site is located in the village of Gvimriani, Lagodekhi Municipality (the land plot is under state ownership cadastral code 54.13.57.223) and covers an area of 23,674 m<sup>2</sup>. The distance from Tbilisi is approximately 130 km. An old school building is located on the land plot designated for the construction of the new school building. As part of this SP, the demolition of the old school building is not planned. It will be fenced off from the construction area and educational activities will continue there. The nearest residential house is about 15 meters away from the land plot allocated for the school. The land plot where the school construction is planned, is a flat area. To the west, it borders a local road, while on the other sides, it is adjacent to privately owned land plots. The area is enclosed by a metal fence.</p> <p>In accordance with the revised scheme of seismic regions of the territory of Georgia, the SP site falls in the 9-point seismic activity zone according to the MSK64 scale (Order of the Minister of Economic Development of Georgia No. 1-1/2284, October 7, 2009).</p> <p>According to the design, the school building will be two-storied with the total area of 2,726.36 m<sup>2</sup> and will accommodate 100 students. The first floor of the school building will comprise the main hallway, the buffet, classrooms for grades 1–5, storage rooms for classrooms, a security room, room with storage and sanitary facilities, a music room, a medical room with an isolation area, a multipurpose room, a resource room, the director's office, boys' and girls' restrooms, staff restrooms, a large multipurpose room, an art and applied arts room, a studio, a school warehouse, and a maintenance room for school infrastructure.</p> <p>The second floor will include classrooms for grades 5–12, storage rooms for classrooms, a staff lounge, a science laboratory with a support storage room, boys' and girls' restrooms, restrooms with universal access, an IT classroom, a library, an advanced IT (information technology) classroom for higher grades, a server room, and a multipurpose hall with lockers.</p> <p>The design ensures a modern, functional, and accessible educational environment, meeting the diverse academic and extracurricular needs of students and staff. In accordance with the design specifications, the entire infrastructure will accommodate individuals with disabilities and other special needs. The</p>



	<p>building will include emergency exits, two stairwells, and one elevator to ensure accessibility and safety.</p> <p>Gvimriani Village is provided with limited utility services, including electricity and natural gas. No potable water supply or wastewater collection and treatment systems are in place. The existing school is supplied with drinking water from a well in the schoolyard. The same well will be used for the new school. Gvimriani Village residents use pit toilets. SP will provide the new school building with the autonomous biological treatment system for sewage management.</p> <p>The SP foresees the implementation of the following works:</p> <ul style="list-style-type: none"> <li>• Preparatory works: Installation of temporary structures such as WCs, lockers for the workers, guard booth, storages for materials as well as household and hazardous waste disposal sites);</li> <li>• Construction of the main building;</li> <li>• Construction of the boiler;</li> <li>• Installation of a biological treatment unit for receiving sewage;</li> <li>• Installation of internal networks for water supply, electricity and gas supply, heating and ventilation networks;</li> <li>• Installation of external gas supply and internet networks and connecting of them to the existing municipal networks;</li> <li>• Installation of fire alarm and firefighting systems;</li> <li>• Arrangement of playgrounds with artificial covers;</li> <li>• Fencing the territory;</li> <li>• Arrangement of parking lots.</li> </ul> <p>There are several trees and bushes in the school yard. According to the design, there is no need to cut them for the construction of the school building, boiler room, playgrounds and paths. As a result of the construction works, it is expected that 1,500 m<sup>3</sup> of cut soil will be generated, of which 500 m<sup>3</sup> will be reused for backfilling and the rest will be removed to a sanitary landfill operated by Solid Waste Management Company of Georgia based on the agreement with this Company or disposed to a site to be allocated by the municipal authority. Also, the removal of 350 m<sup>3</sup> topsoil will be required, which will be temporarily stored on the school territory (construction site) in accordance with the requirements stipulated of the technical regulations approved by the Resolution N424 of the Government of Georgia, dated December 31, 2013, on the Removal, Storage, Use, and Reclamation of Topsoil. After the construction, topsoil will be reused for landscaping of the school area.</p>		
<b>Institutional arrangements (WB)</b>	Task Team Leader: Anna Berdzenadze		Safeguards Specialists: Darejan Kapanadze – <i>Environment</i> Davit Jijelava – <i>Social</i>
<b>Implementation arrangements (Borrower)</b>	Implementing entity: Municipal Development Fund of Georgia	Works supervisor: Company Eptisa Servicios de Ingenieria S.L. Spain	Works contractor: MGD LTD

SITE DESCRIPTION	
<b>Name of institution whose premises are to be Constricted</b>	Public School in village Gvimriani
<b>Address and site location of institution whose premises are to be Constricted</b>	Lagodekhi Municipality, Village Gvimriani Tel: (577) 25 54 20 Email: gvimriani@mes.gov.ge
<b>Who owns the land? Who uses the land (formal/informal)?</b>	The land plot is under the State ownership
<b>Description of physical and natural environment, and of the socio-economic context around the site</b>	<p>Lagodekhi is a municipality in the eastern part of Georgia, located in the region of Kakheti. It is situated on the border with Azerbaijan and is known for its stunning landscapes and biodiversity. The municipality has a population of around 40,000 people and includes the town of Lagodekhi as well as numerous villages. The economy of Lagodekhi is primarily based on agriculture, with the cultivation of grapes, fruits, and vegetables being the main activities. The municipality is also home to the Lagodekhi Protected Areas, which include a national park, a nature reserve, and a protected landscape. These areas are known for their rich flora and fauna, as well as their unique natural features such as waterfalls and canyons.</p> <p>Relief of regional territory is diverse with both flat and mountainous relief. Alazani Valley is in the flat terrain at 240.0-420.0 m above sea level. Mountainous relief is in the North-West part of the territory. It is presented as wrinkled system of south slope of big Caucasus, which average (absolute marks 570-800 m.) and high-mountainous zones (absolute marks up to 2200 m.). Relief is separated with many watery and periodically watery ravines.</p> <p>The study area falls within Climatic Subdistrict II-B according to construction-climate zoning. Average air temperature data are as follows:</p> <ul style="list-style-type: none"> <li>• Annual mean temperature: 12.6°C</li> <li>• Absolute minimum: -23.0°C</li> <li>• Absolute maximum: 38.0°C</li> <li>• Average maximum temperature of the hottest month: 29.9°C</li> <li>• Five-day average minimum during the coldest period: -8.0°C</li> <li>• Daily average minimum during the coldest period: -11.0°C</li> <li>• Average for the coldest period: -0.7°C</li> </ul> <p>The SP land plot and adjacent areas are situated on gently sloping terrain. Based on the morphometric and geomorphological properties, no significant changes in landscape formation or the emergence of new formations due to contemporary geodynamic processes have been observed within the study area or its vicinity.</p>

<b>Locations and distance for material sourcing, especially aggregates, water, stones?</b>	<p>The nearest official landfill for non-hazardous waste is located approximately 20 kilometers from the SP area, in the village Matsimi, Lagodekhi Municipality.</p> <p>The distance from the SP area to the nearest licensed quarry is approximately 10 kilometers, located on the Kabali River.</p>
<b>LEGISLATION</b>	
<b>National &amp; local legislation &amp; permits that apply to project activity</b>	<p>I2Q Project implemented in accordance with the World Bank's safeguard policy OP/BP 4.01 - Environmental Assessment. Based on this policy, present subproject is classified as environmental category "B" and the present ESMP is developed for construction works. According to the principles of OP/BP 4.01 and Environmental and Social Management Framework (ESMF) of I2Q Project.</p> <p>Under the national legislation of Georgia, school construction does not require assessment of an environmental impact and issuance of an Environmental Decision. However, with the national regulation system:</p> <ul style="list-style-type: none"> <li>(i) Construction materials must be obtained from licensed providers.</li> <li>(ii) If the Contractor wants to open a quarry, an appropriate license must be obtained from the National Agency of Minerals Resources under the Ministry of Economy and Sustainable Development.</li> <li>(iii) Suppose over 200 tons of non-hazardous waste or over 1000 tons of inert materials or over 120 kg of hazardous waste is generated annually due to the contractor's activities. In that case, the contractor shall prepare and obtain approval of the Ministry of Environmental Protection and Agriculture (MEPA) on the Waste Management Plan, prepare the report on waste inventory, and appoint an environmental manager, whose identity information should be submitted to the MEPA following the requirements of the Waste Management Code.</li> <li>(iv) Construction waste should be disposed at the official landfill based on the agreement with the Solid Waste Management Company or placed at the pre-selected site officially agreed with local self-government.</li> <li>(v) The topsoil shall be removed and stored in accordance with the requirements stipulated in the Resolution N424 of the Government of Georgia of December 31, 2013, on the Removal, Storage, Use, and Reclamation of Topsoil.</li> </ul>
<b>GRIEVANCE REDRESS MECHANISM</b>	
<p>A grievance redress mechanism (GRM) will be available to allow project-affected people (PAP) appealing any action or decision on which they disagree.</p> <p>PAPs will be informed about the available GRM during public consultations and through distributing of brochures prior to commencement of works. In addition, an announcement with relevant information will be displayed on the information boards in the lobbies of buildings of local municipality. APs will be fully informed of their rights and of the procedures for addressing complaints either verbally or in writing during pre-contraction, construction, and operation periods. Care will always be taken to prevent grievances rather</p>	

than going through a redress process.

Received grievances will be lodged to the MESY and to the MDF. As for grievance monitoring MESY and MDF registers, all received compliances, comments, and how the compliance will be addressed. During public consultations, the local population will be informed about the grievance redress process and received information about contact persons.

The contact person from the MESY is Marine Zhvania (Tel: +995 577 27 88 41, [marina.zhvania@iiq.gov.ge](mailto:marina.zhvania@iiq.gov.ge), 0102 Tbilisi, Dimitri Uznadze N 52);

The contact person from the MDF is David Arsenashvili (Tel: +599 019 183, [feedback@mdf.org.ge](mailto:feedback@mdf.org.ge), 150 Davit Aghmashenebeli ave., 4th floor, 0112 Tbilisi, Georgia)

#### **PUBLIC CONSULTATION**

**Identify when / where the public consultation process will take place**

On April 24, 2025, the MDF and the MESY organized public consultation to discuss the design, Environmental and Social Screening Report, and Environmental and Social Management Plan (ESMP) prepared for the SP for the construction of Gvimriani Public School in Lagodekhi Municipality.

#### **ATTACHMENTS**

- Attachment 1: Ortho Photo
- Attachment 2: General Plan
- Attachment 3: Topo Plan
- Attachment 4: Cadastral Information
- Attachment 5: Cadastral Plan
- Attachment 6: Site photos
- Attachment 7: Design drawings (3D visualization etc.)
- Attachment 8: Minutes of public consultation
- Attachment 9: Agreements/licenses

## PART B: SAFEGUARDS INFORMATION

ENVIRONMENTAL /SOCIAL SCREENING			
Will the site activity include/involve any of the following?	Activity/Issue	Status	Triggered Actions
	1. Rehabilitation	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	If yes, see Section <b>A</b> below
	2. New construction	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	If yes, see Section <b>A</b> below
	3. Individual wastewater treatment system	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	If yes, see Section <b>B</b> below
	4. Historic building(s) and districts	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	If yes, see Section <b>C</b> below
	5. Acquisition of land <sup>1</sup>	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	If yes, see Section <b>D</b> below
	6. Impacts on land and property use	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	If yes, see Section <b>E</b> below
	7. Hazardous or toxic materials <sup>2</sup>	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	If yes, see Section <b>F</b> below
	8. Impacts on forests and/or protected areas	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	If yes, see Section <b>G</b> below
	9. Handling / management of medical waste	<input type="checkbox"/> Yes <input checked="" type="checkbox"/> No	If yes, see Section <b>H</b> below
	10. Traffic and pedestrian safety	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	If yes, see Section <b>I</b> below
	11. Community and labor health and safety	<input checked="" type="checkbox"/> Yes <input type="checkbox"/> No	If yes, see Section <b>J</b> below

<sup>1</sup> Land acquisitions includes displacement of people, change of livelihood encroachment on private property this is to land that is purchased/transferred and affects people who are living and/or squatters and/or operate a business (kiosks) on land that is being acquired.

<sup>2</sup> Toxic / hazardous material includes but is not limited to asbestos, lead-containing and other toxic paints, noxious solvents, etc.

## PART C: MITIGATION MEASURES

ACTIVITY	PARAMETER	MITIGATION MEASURES CHECKLIST
0. General Conditions	Notification and Worker Safety	<ul style="list-style-type: none"> <li>(a) Obtain all legally required permits for construction, extraction, natural construction materials, disposal of waste, and others as relevant.</li> <li>(b) Ensure the supply of personal protective equipment to staff and personnel following good international practice (always hardhats, as needed masks and safety glasses, harnesses, and safety boots), and control its use.</li> <li>(c) Signpost worksites to inform workers of key rules and regulations to follow.</li> <li>(d) Put up information on the company undertaking works at each worksite and provide contact information.</li> <li>(e) Workers' PPE will comply with international good practice (always hardhats, as needed masks and safety glasses, harnesses and safety boots).</li> </ul>
A. General Rehabilitation and /or Construction Activities	Air Quality	<ul style="list-style-type: none"> <li>(a) Keep demolition debris in a controlled area and spray with water to reduce debris dust.</li> <li>(b) Suppress during pneumatic drilling/wall destruction by ongoing water spraying and/or installing dust screen enclosures at the site.</li> <li>(c) Keep the surrounding environment (sidewalks, roads) free of debris to minimize dust.</li> <li>(d) There will be no open burning of construction / waste material at the site.</li> <li>(e) There will be no excessive idling of construction vehicles at sites.</li> <li>(f) Truck loads should be confinement and protected with lining.</li> </ul>
	Noise	<ul style="list-style-type: none"> <li>(a) Limit construction noise to daytime working hours.</li> <li>(b) During operations, the engine covers of generators, close air compressors, and other powered mechanical equipment, and place equipment as far away from residential areas as possible.</li> <li>(c) The maximum allowed speed should be restricted.</li> </ul>
	Water Quality	<ul style="list-style-type: none"> <li>(a) Establish appropriate erosion and sediment control measures such as hay bales and/or silt fences to prevent sediment from moving off-site and causing excessive turbidity in nearby streams and rivers.</li> <li>(b) Wash construction vehicles and machinery only in designated areas where runoff will not pollute natural surface water bodies.</li> <li>(c) Lubricants, fuel and solvents should be stored and used for servicing machinery exclusively in the designated sites, with adequate lining of the ground and confinement of possible operation and emergency spills. Spill containment materials (sorbents, sand, sawing, chips etc.) should be available on construction site.</li> </ul>

	Waste management	<ul style="list-style-type: none"> <li>(a) Minimize the amount of generated waste to the extent possible.</li> <li>(b) Separate various types of generated waste and re-use / recycle relevant types of waste to the possible extent.</li> <li>(c) Allocate sites for temporary on-site storage of various types of waste. Do not allow the accumulation of excessive amounts of waste on-site.</li> <li>(d) Obtain formal arrangements with municipal authorities to dispose of household waste and final placement of excess material (inert construction waste).</li> <li>(e) Make timely arrangements for the disposal or hand-over of hazardous waste to licensed companies.</li> </ul>
	Material supply	<ul style="list-style-type: none"> <li>a) Use existing plants, quarries, or borrow pits with appropriate official approval or valid operating license.</li> <li>b) Obtain licenses for any new quarries and/or borrowing areas if their operation is required;</li> <li>c) Reinstate used sections of quarries and/or borrowing areas as extraction proceeds on or properly closed quarries if extraction completed and license expired.</li> <li>d) Haul materials in off-peak traffic hours.</li> <li>e) Place speed regulating, diverting, and warning signs for traffic as appropriate.</li> </ul>
B. Individual wastewater treatment system	Water Quality	<ul style="list-style-type: none"> <li>a) Ensure that the approach of handling sanitary wastes and wastewater and the design of the treatment system is approved by relevant authorities.</li> <li>b) Ensure that before discharging into receiving waters, effluents from individual wastewater systems are treated in order to meet the minimal quality criteria set out by national guidelines</li> <li>d) on effluent quality and wastewater treatment</li> <li>e) Undertake monitoring of newly established wastewater treatment systems and report to</li> <li>f) Employer on the monitoring outcome</li> <li>g) Wash construction vehicles and machinery only in designated areas where runoff will not pollute natural surface water bodies.</li> </ul>
J. Community and labor health and safety	Earthworks	<ul style="list-style-type: none"> <li>(a) Topsoil should be stripped before starting of earthworks.</li> <li>(b) Proper topsoil storage practice should be applied to ensure to maintain physical-chemical and biological activity of the soil; Temporary protective silt fencing should be erected to avoid erosion (wash down).</li> <li>(c) Stored topsoil should be used for reinstatement and landscaping.</li> <li>(d) Topsoil from the sites, which will not be reinstated to the initial conditions will be distributed carefully on the surrounding area.</li> <li>(e) Topsoil will be reinstated separately from subsoil, with care taken to avoid mixing of the materials. The topsoil reinstatement will be sufficient to restore the fertile depth to the initial</li> </ul>

		<p>conditions as judged by the topsoil strip during visual observation and comparison of the reinstated site and adjacent land. When replacing the topsoil Contractor will program the works such that the areas furthest away from the stockpiles are reinstated first with reinstatement getting progressively closer to the stockpiles, thus reducing the number of vehicle movements over the reinstated topsoil. The reinstated topsoil will then be harrowed, where practical, to protect the stability and promote vegetative growth.</p> <p>(f) In case chance find is encountered in the course of earth works, the contractor must immediately stop any physical activity on site and informs the MDF. The MDF promptly notifies the Ministry of Culture and Monument Protection, which takes over responsibility for the following course of action. Works may resume only upon receipt of written permission from the Ministry of Culture and Monument Protection.</p>
	Public relationship management	<p>(a) Assign a local liaison person within the Contractor's team to communicate with and receive requests/ complaints from the local population.</p> <p>(b) Consult local communities to identify and proactively manage potential conflicts between an external workforce and local people.</p> <p>(c) Raise local community awareness about sexually transmitted disease risks associated with an external workforce and include local communities in awareness activities.</p> <p>(d) Inform the population about construction and work schedules, interruption of services, traffic detour routes and provisional bus routes, blasting, and demolition, as appropriate.</p> <p>(e) Limit construction activities at night. When necessary, ensure that night work is carefully scheduled, and the community is adequately informed about taking essential measures.</p> <p>(f) At least five days in advance of any service interruption (including water, electricity, telephone, bus routes), advise the community through postings at the worksite, at bus stops, and in affected homes/businesses.</p> <p>(g) Address concerns raised through Grievance Redress Mechanism established by the Employer within the designated timeline within the scope of Contractor's liability.</p> <p>(h) To the extent possible, do not locate work camps close to local communities.</p> <p>(i) Undertake siting and operation of worker camps in consultation with neighboring communities.</p>



## PART D: MONITORING PLAN

Activity	What (Is the parameter to be monitored?)	Where (Is the parameter to be monitored?)	How (Is the parameter to be monitored?)	When (Define the frequency / or continuous?)	Why (Is the parameter being monitored?)	Who (Is responsible for monitoring?)
CONSTRUCTION PHASE						
Supply with construction materials	Purchase of construction materials from the officially registered suppliers	In the supplier's office or warehouse	Verification of documents	During the conclusion of the supply contracts	To ensure technical reliability and safety of infrastructure	MDF, Construction supervisor
Transportation of construction materials and waste Movement of construction machinery	Vehicles and machinery are kept in standard technical condition; Truck loads are confined and protected with lining; Established hours and routes of transportation are respected	Construction site	Inspection	Unannounced inspections during work hours and beyond	Limit pollution of soil and air from emissions; Limit nuisance to local communities from noise and vibration; Minimize traffic disruption.	MDF, Construction supervisor, Traffic Police
Earthworks	Temporary storage of excavated material in the pre-defined and agreed upon locations; Backfilling of the excavated material and/or its disposal to the formally designated locations; In case of chance finds immediate suspension of works, notification of the Ministry of Culture and Monument Protection, and resumption of works exclusively upon formal consent of the Ministry. Topsoil is striped before starting of the earthworks;	Construction site	Inspection	In the course of earth works;	Prevent pollution of the construction site and its surroundings with construction waste; Prevent damage and loss of physical cultural resources; Prevent topsoil losses.	MDF, Construction supervisor


	Proper topsoil storage practice is applied; Temporary protective silt fencing is erected; Striped topsoil is used for reinstatement and landscaping.					
Sourcing of the natural construction material	Purchase of material from the existing suppliers if feasible; Obtaining of extraction license by the works contract and strict compliance with the license conditions; Terracing of the borrow area, backfilling to the exploited areas of the borrow site, and landscape harmonization; Excavation of river gravel and sand from outside of the water stream, arrangement of protective barriers of gravel between excavation area and the water stream, and no entry of machinery into the water stream.	Borrowing areas	Inspection of documents Inspection of works	In the course of material extraction	Limiting erosion of slopes and degradation of ecosystems and landscapes; Limiting erosion of riverbanks, water pollution with suspended particles, and disruption of aquatic life.	MDF, Construction supervisor
Generation of construction waste	The temporary storage of construction waste in specially allocated areas; Timely disposal of waste to the formally designated locations	Construction site; Waste disposal site	Inspection	Periodically during construction and upon complaints	Prevent pollution of the construction site and nearby area with solid waste	MDF, Construction supervisor
Traffic disruption	Installation of traffic	At and around	Inspection	In the course of	Prevent traffic	MDF,

and limitation of pedestrian access	limitation/diversion signage; Storage of construction materials and temporary placement of construction waste in a way preventing congestion of access roads	the construction site		construction works	accidents; Limit nuisance to residents	Construction supervisor
Workers' health and safety	Provision of uniforms and safety gear to workers; Provision of potable water and lavatories for men and women at worksite; Informing of workers and personnel on the personal safety rules and instructions for operating machinery/equipment, and strict compliance with these rules/instructions; Adoption and adherence to plan for preventing spread of COVID-19 infection and action in response to the possible outbreak.	Construction site	Inspection	Unannounced inspections in the course of work	The limited occurrence of on-the-job accidents and emergencies	MDF, Construction supervisor
Works within settlement	Informing affecting population on the upcoming works and any temporary disruptions of municipal service provision that may occur during works; Observance of the established working hours during daytime, minimizing noise and dust emissions,	Construction site	Inspection	Recurrent	Ensure the safety of residents and minimize nuisance	MDF, Construction supervisor

	limiting speed of moving construction vehicles and machinery.					
OPERATION PHASE						
Generation of waste from maintenance of school	Proper management of solid waste	Municipal area	Inspection	Throughout operation of the school	Prevent pollution with solid waste	MESY
Operation of sewage biological treatment unit	Providing regular maintenance and timely repair, once required, to the biological treatment unit provided for the school building	School territory	Inspection	During operation of facility	Prevent pollution of surface and ground water with untreated sewage	MESY

[illegible]

### Attachment 3: Topo Plan

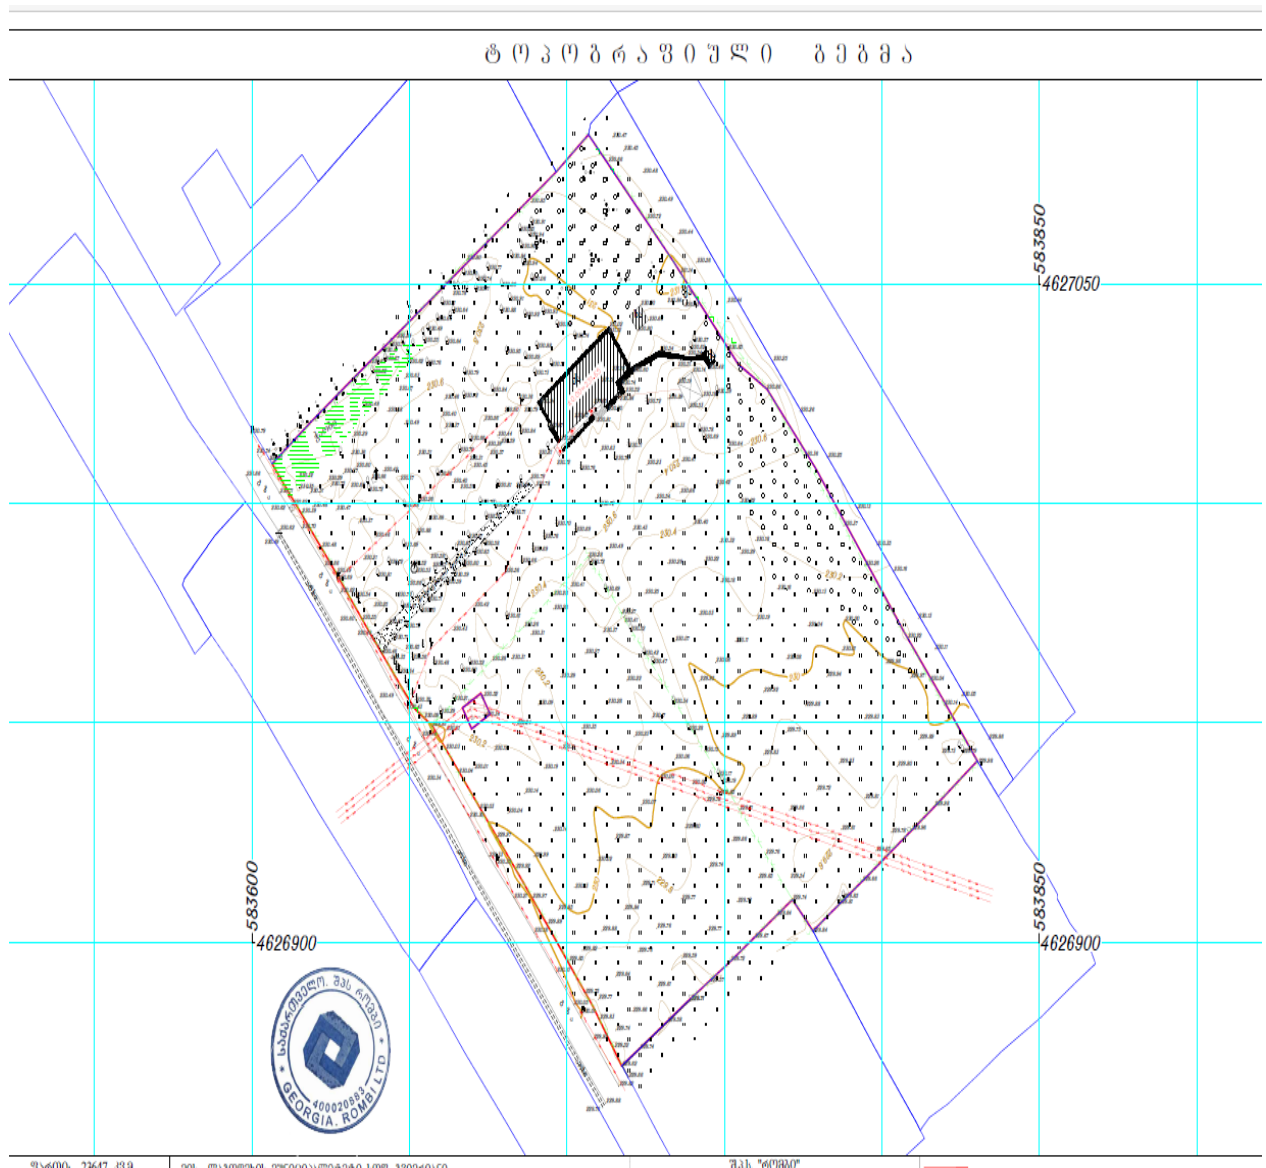





მინის (უძრავი ქონების) საკადასტრო კოდი **N 54.13.57.223**

ამონაწერი საჯარო რეესტრიდან

განცხადების რეგისტრაცია  
**N 892024800149 - 19/11/2024 10:34:14**

მომზადების თარიღი  
**20/11/2024 10:40:19**

საკუთრების განყოფილება

ზონა ლაგოდები	სექტორი აფენი	კვარტალი	ნაკვეთი	ნაკვეთის საკუთრების ტიპი: საკუთრება ნაკვეთის დანიშნულება: არასასოფლო სამეურნეო დაზუსტებული ფართობი: 23647.00 კვ.მ. ნაკვეთის წინა ნომერი: <b>54.13.26.258</b> ; შენობა-ნაგებობის ჩამონათვალი: N01; N02; N03- სამშენებლო დოკუმენტაციის გარეშე
<b>54</b>	<b>13</b>	<b>57</b>	<b>223</b>	
მისამართი: ლაგოდების მუნიციპალიტეტი, სოფელი გვიმრიანი, მე-9 ქუჩა, N 3				

მესაკუთრის განყოფილება

განცხადების რეგისტრაცია : ნომერი 542004000573 , თარიღი 11/08/2004

უფლების დამადასტურებელი დოკუმენტი:

- სისტემური რეგისტრაციის ფარგლებში უძრავი ნივთის ადგილზე დათვალიერების ოქმი N737756 , დამოწმების თარიღი: 06/06/2023 , საჯარო რეესტრის ეროვნული სააგენტო
- უსასყიდლო უზუფრუქტის ხელშეკრულება N1-1842 , დამოწმების თარიღი: 27/10/2006 , ნოტარიუსი ზ. ჩიტიაშვილი
- მომართვა , საქართველოს ეკონომიკური განვითარების სამინისტროს სახელმწიფო ქონების აღრიცხვისა და პრივატიზაციის ლაგოდების სამმართველო
- სარეგისტრაციო ბლოკის გეგმა N021

მესაკუთრები:

სახელმწიფო , ID ნომერი: 203840433

მესაკუთრე:

სახელმწიფო

აღწერა:

იპოთეკა

საკადასტრო გირავნობა:

რეგისტრირებული არ არის

სარგებლობა

განცხადების რეგისტრაცია ნომერი <b>882015459077</b> თარიღი <b>14/08/2015</b> <b>10:35:12</b>	მოსარგებლე: სსიპ ლაგოდების მუნიციპალიტეტის სოფელ გვიმრიანის საჯარო სკოლა 233137352; მესაკუთრე: სახელმწიფო; საგანი: 23153.00 კვ.მ არასასოფლო-სამეურნეო დანიშნულების მინის ნაკვეთი მასზე განთავსებული შენობა-ნაგებობებით; საკადასტრო კოდი 54.13.57.223; არსებობის ვადით;
უფლების რეგისტრაცია: თარიღი <b>18/08/2015</b>	ბრძანება, რეესტრის ნომერი N1/5-394, დამოწმების თარიღი 27/07/2015, სსიპ სახელმწიფო ქონების ეროვნული სააგენტო

ვალდებულება


ყადალა/აკრძალვა:

რეგისტრირებული არ არის

მოვალეობა რეესტრი:

რეგისტრირებული არ არის

## Attachment 5: Cadastral Plan

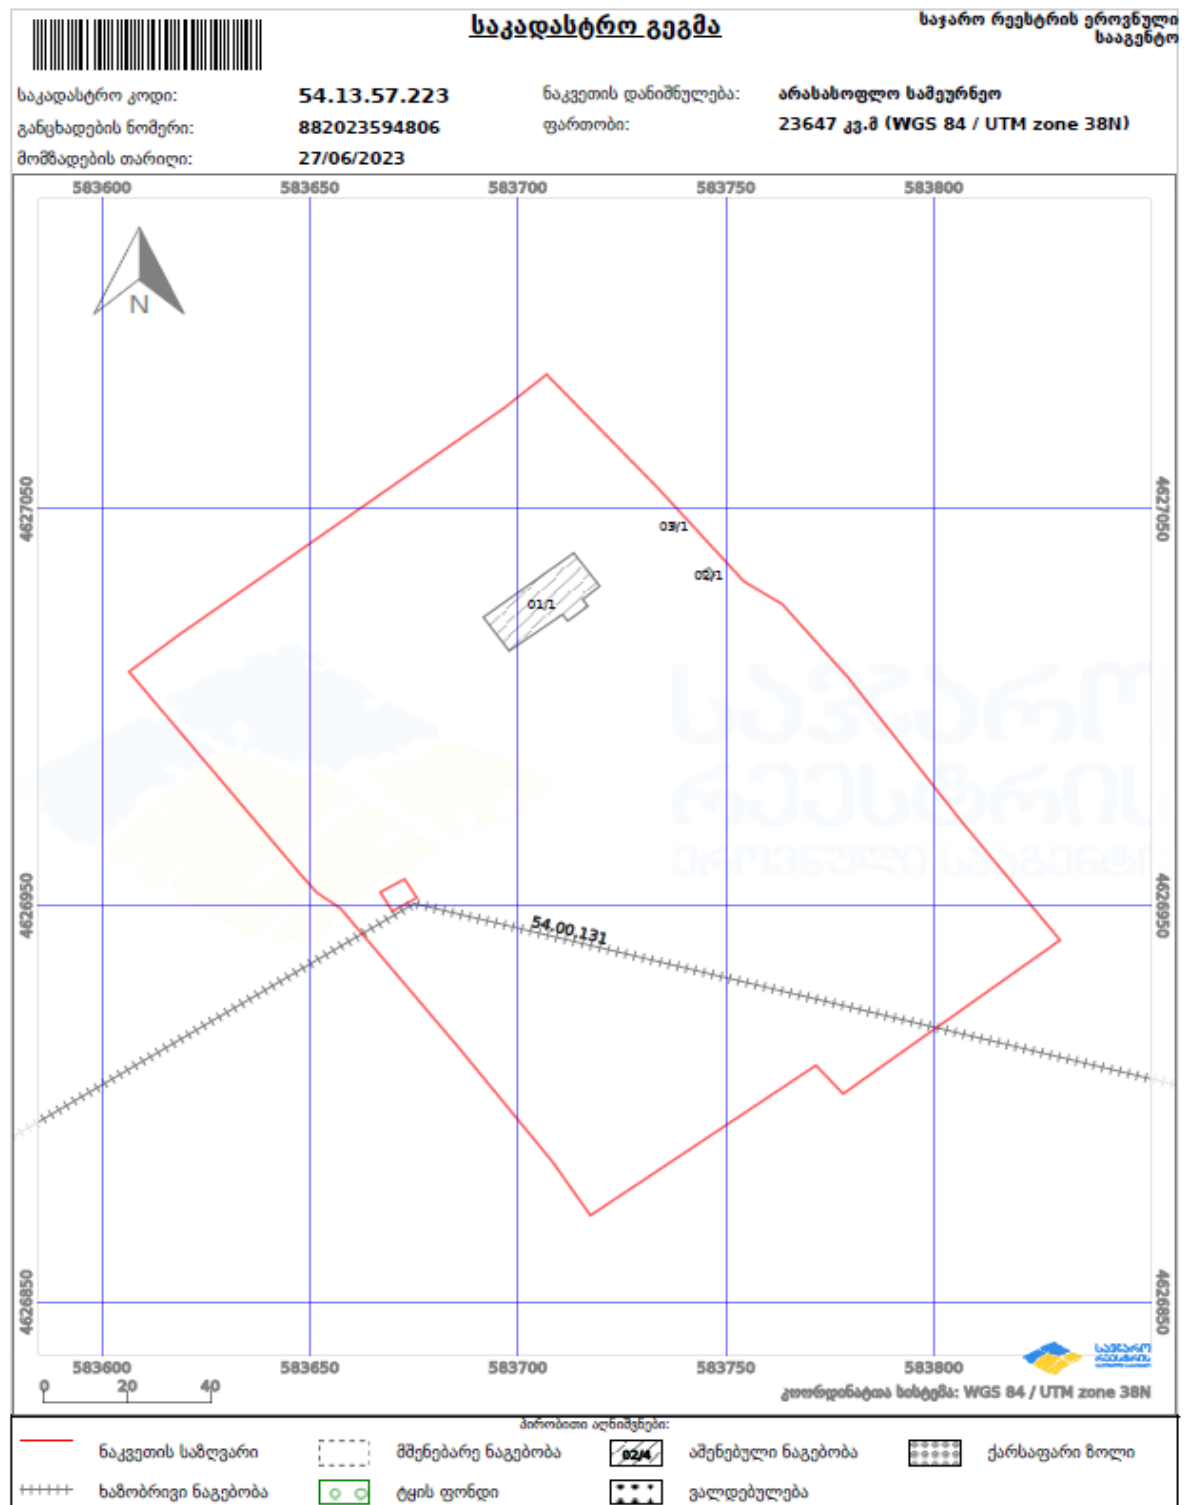



**Attachment 6: Site photos**



**Attachment 7: Design drawings (3D visualization etc.)**



**April 24, 2024**

**Village Gvimriani, Lagodekhi Municipality**

## **Georgia I2Q Project**

### **Construction of Gvimriani Public School in Lagodekhi Municipality Public Consultation meeting**

#### **on the draft Environmental and Social Screening Report and Environmental and Social Management Plan**

On April 24, 2025, the Municipal Development Fund of Georgia (MDF) and the Ministry of Education, Science and Youth of Georgia (MESY) organized public consultation to discuss the design, Environmental and Social Screening Report, and Environmental and Social Management Plan (ESMP) prepared for the sub-project “Construction of Gvimriani Public School in Lagodekhi Municipality”. The meeting was held in Gvimriani Public School. The specific place was selected according to the project specification. Consultation meeting details (date, time and contact information) were included in the announcement. The announcements were posted on the streets near the SP territory, as well as on the school information board and on the websites of the MDF and MESY.

The consultation aimed to inform the interested parties about the SP, scheduled works under the SP, its potential negative/positive impacts on the natural and social environment, and their prevention or mitigation measures.

#### **Those present at the meeting from the Gvimriani Public School:**

██████████ – Director of the school

██████████ – Head of the resource center.

Teachers, parents and pupils of the school

#### **Representatives of MESY:**

██████████ – GRM contact person

#### **Representatives of the Municipal Development Fund of Georgia:**

██████████ – Environmental Specialist

██████████ – Social and Gender specialist

██████████ opened the meeting and presented representatives of the MDF and MESY and the meeting objectives. ██████ briefly introduced SP and discussed in detail all the construction and demolishing works planned under the SP.

█████ explained that according to the Environmental Assessment Code of Georgia, the SP does not require the Environmental Decision from the Ministry of Environmental Protection and Agriculture (MEPA). However, to ensure the SP's environmental and social safety, MDF is responsible for following the World Bank (WB) safeguard policies. Therefore, █████ presented the WB's social and environmental screening procedures and presented the ESMP elaborated for this SP.

█████ briefly discussed ESMP's content and structure. █████ presented the environmental, social, public relations, and labor-management measures described in the document. As an essential part of the ESMP, █████ informed the attendees about potential environmental and social risks associated with this SP and mitigation measures to prevent or minimize those negative impacts.

█████ mentioned that according to the design, no tree cutting is required, excavated soil will be fully reused on site territory for yard landscaping.

█████ noted that ESMP forms an integral part of the civil works contract. Therefore, thorough implementation of ESMP provisions aimed at protecting the social and natural environment and human health, is obligatory for the work contractor. ███ also discussed the environmental monitoring aspects, responsible parties for the environmental supervision, and reporting procedures during the SP implementation.

█████ mentioned that the SP implementation does not necessitate land take or resettlement, or the economic displacement (for example, for formal or informal vendors). ███ informed the participants about procedures and the importance of the Grievance Redress Mechanism established at MDF. Shared information about contact persons for communication, in case of existence of any complaints concerning environmental or social issues and/or expressing the comments and suggestions. ███ provided information regarding billboards where they can find GRM contact information (phone numbers and emails), complaint boxes that will be available at every construction site and grievance forms for anonymous complaints. ███ distributed brochures with GRM contact information through the audience.

█████ presented information on public engagement, feedback mechanisms and gender-related aspects of SP implementation. Leaflets with information on handling sexual harassment and gender-based violence were distributed among the participants.


At the end of the meeting, the audience participated in a Q&A session. The following questions were entertained:

Questions and Remarks:	Answers and Comments:
When will we have the new school?	Construction works will be completed in the end quarter of 2026.
When will school construction begin?	Construction works begin in May.
What fate awaits the existing school building, and will the teaching process continue in parallel with the construction?	During the construction works, the teaching process will continue in the existing school building. The existing building will not be demolished but rather fenced off to prevent pupils' access for their safety.

The participants expressed their gratitude and noted that the implementation of this SP is highly important and the priority for the pupils, teachers, parents, and local population.

Attendees expressed their positive attitude towards the SP.

**Photo materials are enclosed:**





List of Attendees:

სოფელი გვიმრიანის საჯარო სკოლის მშენებლობა (ლაგოდეხის მუნიციპალიტეტი)


Construction of the village Gvimriani Public School (Lagodekhi Municipality)


შეხვედრაზე დამსწრეთა რეგისტრაციის ფურცელი


Public Consultation Meeting

List of Attendees

#	სახელი და გვარი / Full Name	მისამართი / Address	ორგანიზაცია / Organization	საკონტაქტო ინფორმაცია / Contact Information	ხელმოწერა / Signature











Present minutes were prepared by MDF in April 2025.

Attachment 9: Agreements/licenses  
Agreement for supply of inert materials

**ხელშეკრულება**

ქ. თბილისი 14 აგვისტო 2024 წელი

ერთი მხრივ შპს „ა. კე“-ს (შემდგომში „მიმწოდებელი“) წარმომადგენელი მისი დირექტორის [REDACTED] სახით და მეორეს მხრივ შპს „მგდ“-ს (შემდგომში „დამკვეთი“) წარმომადგენელი მისი დირექტორის [REDACTED] სახით, ვდებთ წინამდებარე ხელშეკრულებას (შემდგომში - ხელშეკრულება) შემდეგზე:

**1. ხელშეკრულების საგანი**

მიმწოდებელი იღებს ვალდებულებას, დამკვეთის მოთხოვნის და შესაბამისი ღირებულების გადახდის შემდეგ მიაწოდოს მას ინერტული მასალა ქვიშა-ხრემი ლაგოდების მუნიციპალიტეტში მდებარე სოფელ ყარაჯალის და სოფელ გვიმრიანის საჯარო სკოლების რეაბილიტაციისთვის.

**2. ხელშეკრულების ღირებულება**

2.1. 10<sup>3</sup> ქვიშა ხრემის ღირებულება ადგილზე დატვირთვით შეადგენს 35 -ლარს დღგს ჩათვლით.

**3. ანგარიშსწორების ფორმა და ვადები**

3.1. მიმწოდებელთან ანგარიშსწორება განხორციელდება უნაღდო ანგარიშსწორების ფორმით ერვნულ ვალიუტაში.

3.2. მიმწოდებელთან ანგარიშსწორება იწარმოებს მიწოდებული ინერტული მასალის შესაბამისად 5 სამუშაო დღეში.

**4. საქონლის მიწოდების ადგილი და ვადა**

4.1 ლაგოდების მუნიციპალიტეტი

4.2 ხელშეკრულება ძალაშია 2026 წლის 1 ოქტომბრამდე

**5. მხარეთა უფლება მოვალეობები**

5.1 შემსყიდველი უფლებამოსილია წებისმიერ დროს განახორციელოს მიმწოდებლის მიერ ნაკისრი ვალდებულებების შესრულებისა და ხარისხის ინსპექტირება.

5.2 შემსყიდველი ვალდებულია უზრუნველყოს მიწოდებული პროდუქციის ღირებულების ანაზღაურება ხელშეკრულებით გათვალისწინებულ ვადებში.

## 6. კონფიდენციალურობა

- 6.1 მხარეთა მიერ ურთიერთთანამშრომლობის შედეგად მოპოვებული ინფორმაცია წარმოადგენს კონფიდენციალურ ინფორმაციას და არ დაიშვება წინამდებარე ხელშეკრულების პირობების გაცნობა შესაძლე პირთათვის, მეორე მხარის წინასწარი წერილობითი თანხმობის გარეშე. აგრეთვე მხარეებმა უნდა უზრუნველყონ ხელშეკრულების შესრულებისათვის გამოიზნული კორესპონდენციისა და სხვა საქმიანი დოკუმენტაციის შესაძლე პირთაგან დაცვა.
- 6.2 მხარეთა ეს მოვალეობა ძალაშია ხელშეკრულების შეწყვეტის შემდეგაც.
- 6.3 კონფიდენციალური ინფორმაციის ნებისმიერი სახით შესაძლე პირთათვის გადაცემის შემთხვევაში (გარდა კანონმდებლობით გათვალისწინებული შემთხვევებისა) დამოღვევი მხარე ვალდებულია გადაუხადოს მეორე მხარეს პირგასამტეხლო, პირგასამტეხლოს ოდენობა განსაზღვრული იქნება მეორე მხარის მიერ.

## 7 ფორს-მაჟორი

- 7.1 წინამდებარე ხელშეკრულების დარღვევად არ ჩაითვლება შემთხვევა, როცა რომელიმე მხარე ვერ ახერხებს თავისი მოვალეობების შესრულებას ფორს-მაჟორული (დაუძლეველი) გარემოების ზემოქმედების გამო;
- 7.2 ფორს-მაჟორული გარემოებების აღმოფხვრის შემდგომ მხარეები შეთანხმდებიან ხელშეკრულებით ნაკისრი ვალდებულებების შესრულების ახალ ვადებზე. მოქმედი კანონმდებლობის შესაბამისად.


## 8 დავათა გადაწყვეტა

- 8.1 წინამდებარე ხელშეკრულება განიმარტება საქართველოს მოქმედი კანონმდებლობის შესაბამისად.
- 8.2 მხარეთა შორის დავა წყდება ურთიერთმოლაპარაკების საფუძველზე. შეთანხმების მიუღწევლობის შემთხვევაში, მხარეთა შორის დავა წყდება სასამართლოს წესით საქართველოს კანონმდებლობის შესაბამისად.

## 9. ხელშეკრულების მოქმედების ვადები

- 9.1 წინამდებარე ხელშეკრულება ძალაში შედის ორივე მხარის მიერ ხელმოწერის თარიღიდან და მოქმედებს 2026 წლის 1 ოქტომბრამდე.

## 10. შპარეთა რეკვიზიტები და ხელმოწერები

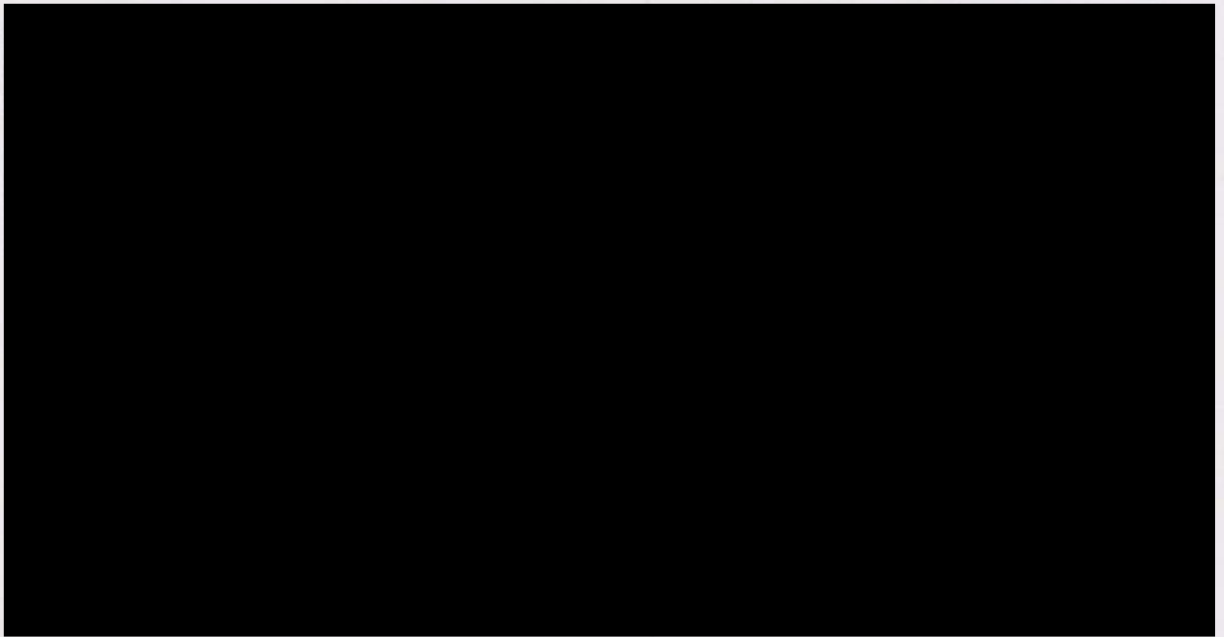



საჯარო სამართლის იურიდიული პირი  
მინერალური რესურსების ეროვნული  
სააგენტო



KA020120398869523

თბილისი, დავით აღმაშენებლის გამზ. №150 ტელ: 0 32 2 95 00 30

ლიცენზია - ბრძანება

22 / თებერვალი / 2023 წ.

შპს „ალ.კე“-ზე სასარგებლო წიაღისეულის მოპოვების ლიცენზიის  
გაცემის შესახებ

„ლიცენზიებისა და ნებართვების შესახებ“ საქართველოს კანონის მე-5 მუხლის, მე-7 მუხლის პირველი პუნქტის, საქართველოს მთავრობის 2005 წლის 11 აგვისტოს №136 დადგენილებით დამტკიცებული „სასარგებლო წიაღისეულის მოპოვების ლიცენზიის გაცემის წესისა და პირობების შესახებ“ დებულების, „სასარგებლო წიაღისეულით სარგებლობის ლიცენზიის გაცემის მიზნით აუქციონის გამართვის, ლიცენზიის გაცემის საწყისი ფასის განსაზღვრისა და ანგარიშსწორების წესის შესახებ დებულების დამტკიცების თაობაზე“ სსიპ მინერალური რესურსების ეროვნული სააგენტოს უფროსის 2022 წლის 2 მარტის №1 და 2022 წლის 30 დეკემბრის №1442/ს ბრძანებების, 2023 წლის 25 იანვარს ჩატარებული ელექტრონული აუქციონის (აუქციონის შედეგად პირველ ობიექტზე გამარჯვებული გახდა შპს „ალ.კე“ (განაცხადის №4940TH123), ლიცენზიით გათვალისწინებული მოსაპოვებელი ქვიშა-ხრეშის ჯამური მოცულობა (ორივე უბანზე ერთად) 98 970 მ<sup>3</sup>, ლიცენზიის მოქმედების ვადა 5 წელი, ლიცენზიისთვის გადახდილი ფასი 72988.30 ლარი) შედეგებისა და სსიპ - მინერალური რესურსების ეროვნული სააგენტოს მიერ მომზადებული გეოსაინფორმაციო პაკეტის საფუძველზე,

ბ რ ძ ა ნ ე ბ ა :

1. გაიცეს შპს „ალ.კე“-ზე ლაგოდეხის მუნიციპალიტეტში, კაბალის ადმინისტრაციული ერთეულის ტერიტორიაზე, მდ. კაბალის ქვიშა-ხრეშის მოპოვების მიზნით სასარგებლო წიაღისეულის მოპოვების ლიცენზია 5 წლის ვადით შემდეგი პირობების გათვალისწინებით:

ა) დაუწესდეს მიწისა და სამთო მინაკუთვნი (I უბანი ფართობით 23 770 კვ.მ; II უბანი ფართობით 9 220 კვ.მ) დანართით განსაზღვრული X და Y კოორდინატების ფარგლებში;

ბ) ქვიშა-ხრეშის (P კატეგორია) ჯამური მოცულობა (ორივე უბანზე ერთად) ლიცენზიის მოქმედების პერიოდში განისაზღვროს 98 970 მ<sup>3</sup>-ის ოდენობით;

გ) სასარგებლო წიაღისეულის მოპოვება უნდა განხორციელდეს წინასწარ შედგენილი წიაღით სარგებლობის პროექტის მიხედვით;

დ) სასარგებლო წიაღისეულის მოპოვება უნდა წარიმართოს მდინარის კალაპოტის გასწორებაზე მიმართულებით;

ე) გეოდინამიკური სიტუაციის გართულების თავიდან აცილების მიზნით ობიექტის მთელ ფართობზე, წელიწადში ინერტული მასალის მოპოვების სიღრმე (სიმძლავრე) არ უნდა აღემატებოდეს 1.5 მეტრს;

ვ) ლიცენზიის მფლობელი ვალდებულია, მოპოვებული სასარგებლო წიაღისეულის ტრანსპორტირება განახორციელოს ძარაგადახურული ავტომობილებით, ასევე დასახლებულ პუნქტებში სასარგებლო წიაღისეულის ტრანსპორტირებისას უზრუნველყოს საავტომობილო გზის პერიოდული მორწყვა, რათა თავიდან იქნეს აცილებული მტვრის გაფრქვევა დასახლებულ პუნქტებში;

ზ) ლიცენზიის მფლობელი ვალდებულია არ დააზიანოს შიდა სასოფლო გზები, ხოლო დამიანების შემთხვევაში მოახდინოს მისი აღდგენა-რეაბილიტაცია, ლიცენზიის მფლობელს წიაღისეულის მოპოვების



პერიოდში ეკრძალება გზის გვერდულებზე მასალის დასაწყობება, სამშენებლო ნარჩენების დაყრა, მანქანა-მექანიზმების გაჩერება და დგომა;

თ) ლიცენზიის მფლობელი ვალდებულია უზრუნველყოს სალიცენზიო მიწის ნაკვეთზე დაზიანებული ნიადაგის (ასეთის არსებობის შემთხვევაში) რეკულტივაციის ღონისძიებების ჩატარება;

ი) ექსპლუატაციისას მწყრული პროცესების გააქტიურების დროს (ასეთის არსებობის შემთხვევაში) უნდა მოხდეს სამუშაოების შეჩერება, სათანადო ღონისძიებების დასახვა და განხორციელება, გეოდინამიკური სიტუაციის გათვალისწინებით (ასეთის არსებობის) შემთხვევაში, უნდა შესრულდეს უფლებამოსილი სახელმწიფო ორგანოების შესაბამისი მითითებები;

კ) ობიექტის დამუშავება უნდა მოხდეს ქვეყანაში მოქმედი სამთო საქმისთვის მიღებული ტექნიკური უსაფრთხოების ნორმების და წესების დაცვით, ობიექტის დამუშავების დროს მოხსნილი ნიადაგის ფენა და ფუჭი ქანი (ასეთის არსებობის შემთხვევაში) უნდა დასაწყობდეს ტერიტორიის რეკულტივაციის მიზნით მისი შემდგომი გამოყენებისათვის;

ლ) ლიცენზიის მფლობელმა დაიცვას „ტექნიკური რეგლამენტების - წიაღით სარგებლობასთან დაკავშირებული სალიცენზიო პირობების დაცვის შესახებ ანგარიშგების (საინფორმაციო ანგარიშის) წესის, წიაღით სარგებლობის ობიექტის დამუშავების პროექტის, წიაღით სარგებლობის ობიექტის დამუშავების ტექნოლოგიური სქემისა და წიაღისეულის შესწავლის სამუშაოთა გეგმების შედგენის წესისა და სტატისტიკური დაკვირვების ფორმების ( № 1-01, 1-02, 1-03, 1-04) დამტკიცების თაობაზე“ საქართველოს მთავრობის 2014 წლის 4 აპრილის № 271 და „კარიერების უსაფრთხოების შესახებ ტექნიკური რეგლამენტის დამტკიცების თაობაზე“ საქართველოს მთავრობის 2013 წლის 31 დეკემბრის № 450 დადგენილებებით გათვალისწინებული მოთხოვნები;

მ) ლიცენზიის მფლობელი ვალდებულია სასარგებლო წიაღისეულის მოპოვების დაწყებამდე შეადგინოს წიაღით სარგებლობის საპროექტო დოკუმენტაცია ამ ლიცენზია-ბრძანების პირველი პუნქტის „ლ“ ქვეპუნქტში მითითებული ტექნიკური რეგლამენტის მოთხოვნების შესაბამისად;

ნ) ლიცენზიის მფლობელმა ყოველწლიურად 1 აპრილიდან 1 მაისამდე ლიცენზიის გამცემ ორგანოში წარადგინოს წერილობითი ანგარიშგება სალიცენზიო პირობების დაცვის შესახებ;

ო) ლიცენზიის მფლობელი ვალდებულია ამ ლიცენზია-ბრძანების ჩაბარებიდან ერთი თვის ვადაში ლიცენზიის გამცემ ორგანოში დასამტკიცებლად წარადგინოს სასარგებლო წიაღისეულის ათვისების შესაბამისი გეგმა (ყოველწლიურად ასათვისებელი მოცულობის მითითებით);

პ) ლიცენზიის მფლობელმა შეასრულოს საქართველოს მოქმედი კანონმდებლობით დადგენილი მოთხოვნები, მათ შორის „გარემოს დაცვის შესახებ“, „ბუნებრივი რესურსებით სარგებლობისათვის მოსაკრებლების შესახებ“ და „წიაღის შესახებ“, საქართველოს კანონებით და შესაბამისი კანონქვემდებარე აქტებით დადგენილი სხვა მოთხოვნები. ამასთან, „წიაღის შესახებ“ საქართველოს კანონის მე-13 მუხლის პირველი პუნქტის „თ“ ქვეპუნქტის შესაბამისად, წიაღით სარგებლობისას იშვიათი მეცნიერული ან ესთეტიკური ფასეულობის ობიექტების აღმოჩენის შემთხვევაში შეაჩეროს სამუშაოები და დაუყოვნებლივ აცნობოს ამის შესახებ შესაბამის სახელმწიფო ორგანოებს;

ჟ) ლიცენზიის მფლობელი ვალდებულია დაიცვას ასევე სსიპ - მინერალური რესურსების ეროვნული სააგენტოს სასარგებლო წიაღისეულის მართვის დეპარტამენტის № 1702, 26.08.2022 წ. (ID\_59818\_54618) სამსახურებრივი ბარათით წარმოდგენილი გეოსაინფორმაციო პაკეტის საფუძველზე დადგენილი პირობები.

2. ლიცენზია-ბრძანება გასაცნობად გადაეცეს დაინტერესებულ პირს.

3. ლიცენზია-ბრძანება შეიძლება გასაჩივრდეს დაინტერესებული მხარის მიერ მისი ოფიციალური წესით გაცნობის დღიდან ერთი თვის ვადაში, საქართველოს ეკონომიკისა და მდგრადი განვითარების სამინისტროში (ქ. თბილისი, სანაპიროს ქუჩა №2).

სსიპ მინერალური რესურსების ეროვნული სააგენტოს უფროსი

მომსახურების ხელშეკრულება N10

ქ. თბილისი

05.03.2025

შპს „საქართველოს მყარი ნარჩენების მართვის კომპანია“, წარმოდგენილი მისი დირექტორის [REDACTED] სახით, (შემდგომში წოდებული როგორც „შემსრულებელი“) ერთის მხრივ და მეორეს მხრივ შპს „მგდ“ წარმოდგენილი მისი დირექტორის [REDACTED] სახით, (შემდგომში წოდებული როგორც „დამკვეთი“) საქართველოს მოქმედი კანონმდებლობისა და საწარმოს წესდების მე-8 მუხლის მე-8 პუნქტის შესაბამისად, ურთიერთ შეთანხმების საფუძველზე დებენ ხელშეკრულებას შემდეგზე:

1.1 შემსრულებელი ორგანიზაცია 2023 წლის 29 დეკემბრის N86-ო ბრძანების საფუძველზე, ახორციელებს იურიდიული და/ან ფიზიკური პირების მიერ წარმოქმნილი სამშენებლო და ნგრევის შედეგად მიღებული ნარჩენის განთავსების მომსახურებას შემსრულებლის ბალანსზე არსებული ქ.ლაგოდეხისა და ქ.ჩოხატაურის არასახიფათო ნარჩენების ნაგავსაყრელზე (შემდგომში – მომსახურება).

მუხლი 2. ხელშეკრულების პირობები

2.1 შემსრულებელი ვალდებულია დროულად და ხარისხიანად მოემსახუროს დამკვეთს და უზრუნველყოს ხელშეკრულების 1.1 პუნქტში აღნიშნული მომსახურების გაწევა.

მუხლი 3. მხარეთა უფლება-მოვალეობები

3.1 შემსრულებლის უფლება-მოვალეობები:

3.2 დროულად და ხარისხიანად განახორციელოს 1.1 მუხლში აღნიშნული მომსახურება.

3.3 მომსახურების გაწევისას დაიცვას საერთაშორისო სტანდარტებითა და ტექნიკური რეგლამენტებით განსაზღვრული პირობები.

3.4 ხელშეკრულებით განსაზღვრულ ვადაში დამკვეთისაგან მოითხოვოს მომსახურების ღირებულების დროულად გადახდა.

3.5 დამკვეთისაგან მოითხოვოს წინამდებარე ხელშეკრულების პირობების დაცვა.

3.6 დამკვეთის უფლება-მოვალეობები:

3.7 ხელშეკრულების მოქმედების პერიოდში მოითხოვოს შემსრულებლისაგან წინამდებარე ხელშეკრულების პირობების დაცვა.

3.8 ხელშეკრულებით განსაზღვრულ ვადაში და პირობებით გადაუხადოს შემსრულებელს მომსახურების ღირებულება.

3.9 შემსრულებლის კუთვნილ არასახიფათო ნარჩენების ნაგავსაყრელზე ნარჩენის შემოტანა უზრუნველყოს სახანძრო და უსაფრთხოების ნორმების დაცვით.

მუხლი 4. ანგარიშსწორება და ხელშეკრულების ღირებულება

4.1 1 (ერთი) ტონა იურიდიული და/ან ფიზიკური პირების მიერ წარმოქმნილი სამშენებლო და ნგრევის შედეგად მიღებული ნარჩენის განთავსების მომსახურების ღირებულება შეადგენს 10 (ათი) ლარს დღე-ს ჩათვლით.

4.2 დამკვეთი ვალდებულია მიღებული მომსახურების თანხა ჩარიცხოს შემსრულებლის საბანკო ანგარიშზე შესაბამისი ანგარიშ-ფაქტურის ატვირთვიდან 10 (ათი) კალენდარულ დღეში.

4.3 შემსრულებლის მიერ წინამდებარე ხელშეკრულებით ნაკისრი ვალდებულებების შესრულების შემდეგ მხარეები ადგენენ ნარჩენების განთავსების აქტს.

4.4 შემსრულებლის მხრიდან ნარჩენების განთავსების აქტს ხელს აწერს შემსრულებლის სტრუქტურული ერთეულის - რეგიონული მართვის დეპარტამენტის თანამშრომელი შესაბამის რეგიონში.

მუხლი 5. ხელშეკრულების მოქმედების ვადა და მისი შეწყვეტის წესი



5.1 წინამდებარე ხელშეკრულება ძალაში შედის მხარეთა მიერ მისი ხელმოწერის მომენტიდან და მოქმედებს მხარეთა მიერ ნაკისრი ვალდებულებების სრულად და ჯეროვნად შესრულებამდე - 2025 წლის 31 დეკემბრის ჩათვლით.

5.2 ხელშეკრულების ვადამდე შეწყვეტა მხარეებს არ ათავისუფლებთ ხელშეკრულების შეწყვეტამდე შესასრულებელი ვალდებულების შესრულების მოვალეობისაგან.

#### **მუხლი 6. სადავო საკითხების მოგვარება**

6.1 დამკვეთსა და შემსრულებელს შორის წინამდებარე ხელშეკრულების რეალიზაციისას წარმოშობილი სადავო საკითხები წესრიგდება მხარეთა შეთანხმებით, ხოლო შეთანხმების მიუღწევლობის შემთხვევაში სადავო საკითხს განიხილავს სასამართლო.

#### **მუხლი 7. დასკვნითი დებულებები**

7.1 წინამდებარე ხელშეკრულების ყველა მუხლი და დანართი წარმოადგენს მის განუყოფელ ნაწილს. ხელშეკრულებაში ცვლილების შეტანა შეიძლება მოხდეს მხარეთა შეთანხმებით მხოლოდ წერილობით.

7.2 ხელშეკრულების მხარეები თანხმდებიან მასზედ, რომ იმ შემთხვევაში, თუ შემსრულებელი ორგანიზაციის 2023 წლის 29 დეკემბრის N86-ო ბრძანების დანართში, რომლითაც რეგულირდება შესატანი ნარჩენის სახეობები და საფასური შევა რაიმე სახის ცვლილება, ხელშეკრულება დაკორექტირდება შესაბამისად.

7.3 წინამდებარე ხელშეკრულება შედგენილია 2 (ორი) თანაბარი იურიდიული ძალის მქონე ეგზემპლარად ქართულ ენაზე. ერთი ეგზემპლარი გადაეცემა დამკვეთს, ხოლო ერთი ეგზემპლარი ინახება შემსრულებელთან.

#### **მუხლი 8. მხარეთა რეკვიზიტები და ხელმოწერები:**

